


# RiverRenew Executive Dashboard // Month Ending: February 28, 2019



## Program Schedule

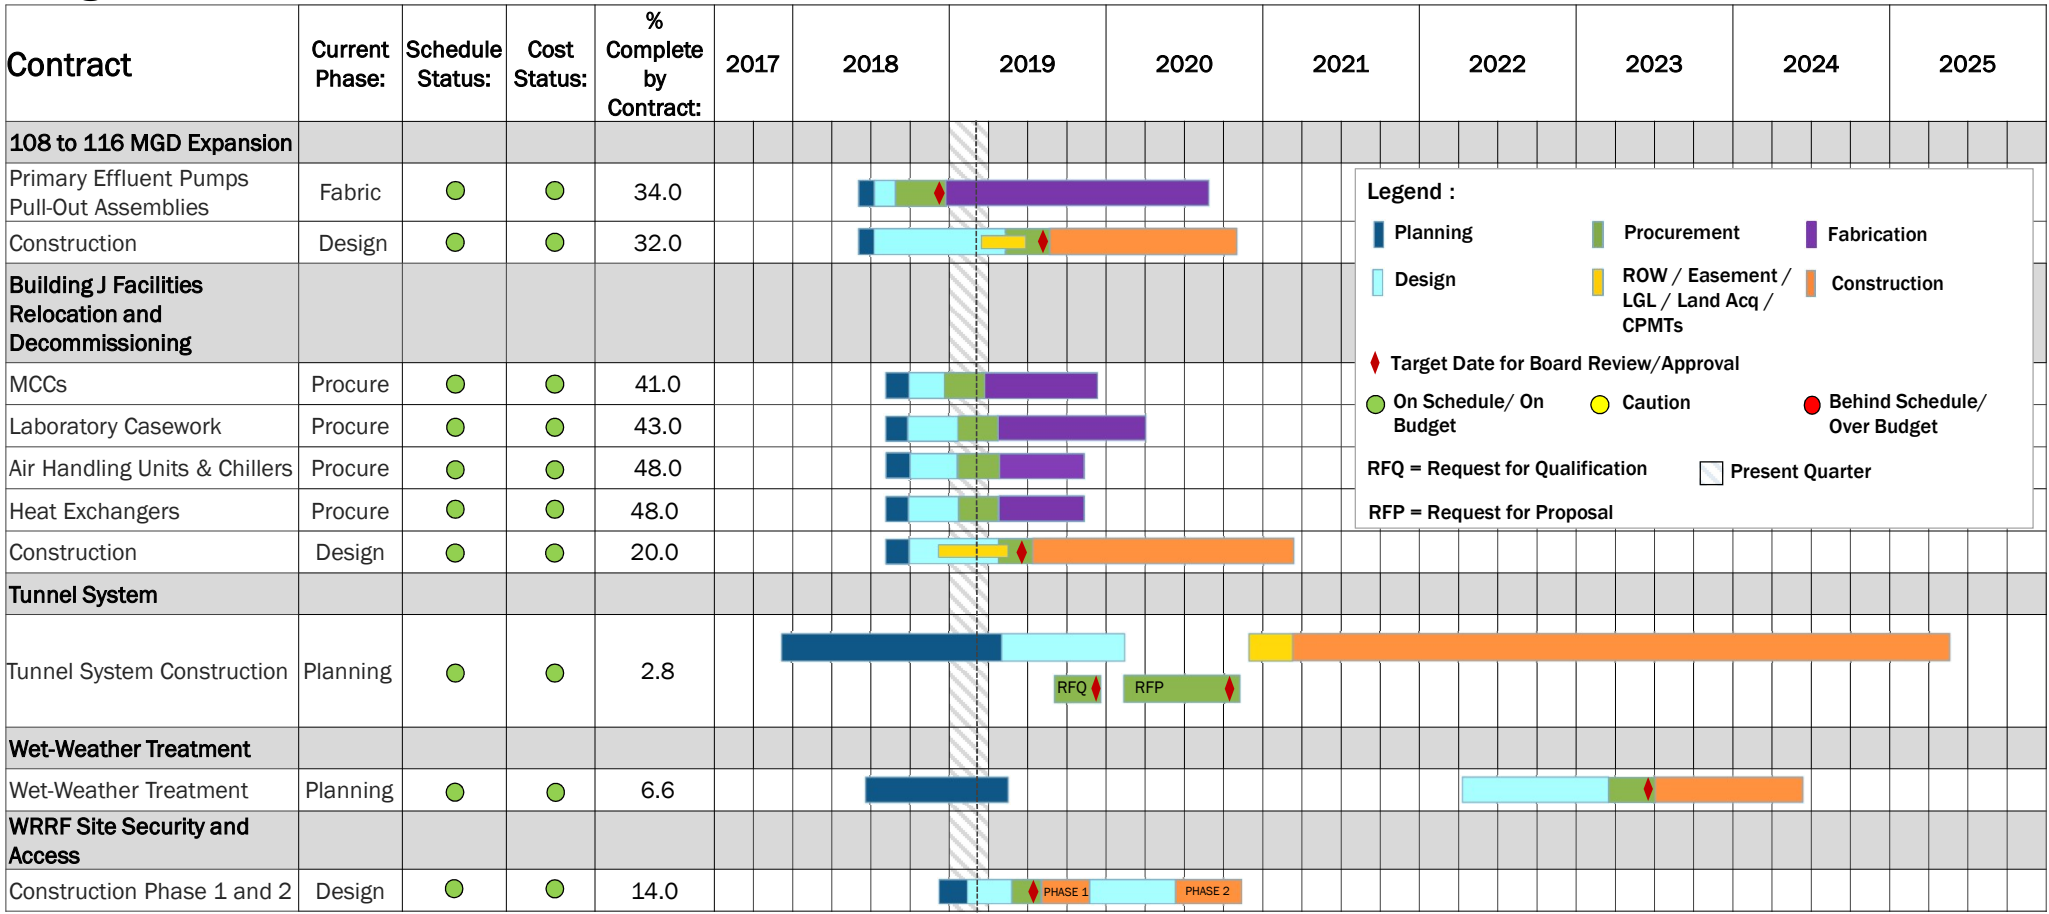

February 28, 2019


## Contract Award Status

Contract	Contract No.:	Date of Contract Award:	Vendor:	Contract Amount:	Notice to Proceed:	Construction Start Date:	Construction Finish Date:
<b>108 to 116 MGD Expansion</b>							
Primary Effluent Pumps Pull-Out Assemblies	19-001	12/19/2018	Flowserve	\$941,911	12/20/2018	12/21/2018	9/12/2019
<b>Building J Facilities Relocation and Decommissioning</b>							
MCCs	19-016	2/26/2019	Rxel	\$280,453.18	2/27/2019	2/27/2019	10/30/2020


# RiverRenew Executive Dashboard // Month Ending: February 28, 2019



## Project to Date Cost by Phase\*

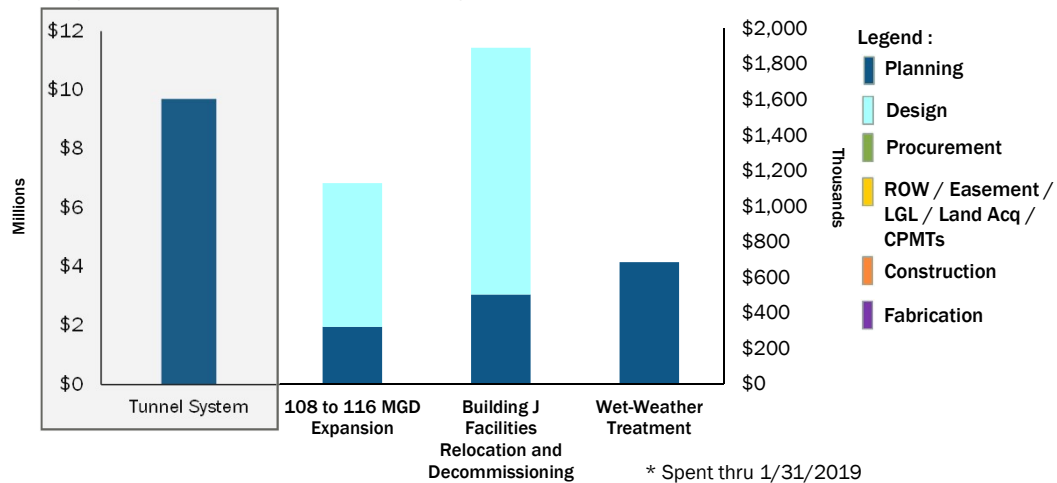

## RiverRenew Spent to Date by Locality\*

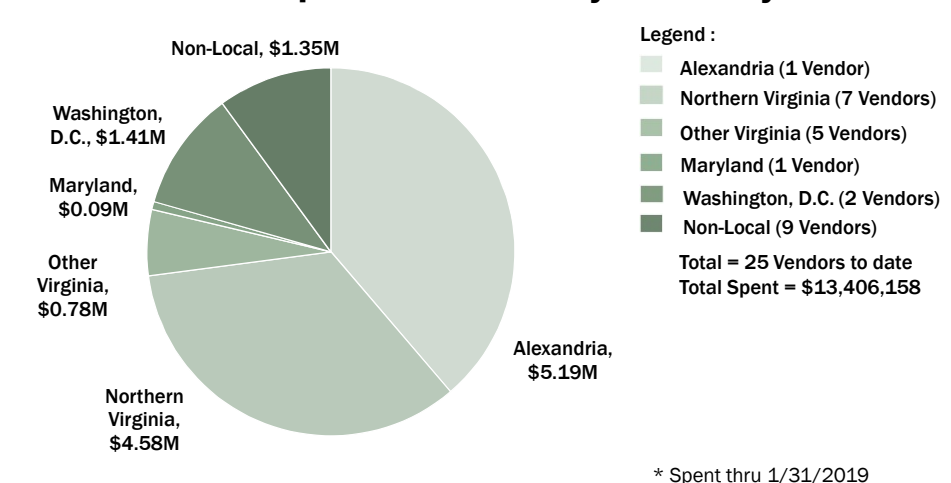

## RiverRenew Cashflow Analysis\*

